

Sierra Valley Groundwater Basin Sustainable Groundwater Management Act (SGMA) Implementation 2019-2022 SCHEDULE OF ACTIVITIES

Acronyms:

- PT= GSP Project Team
 - GSA= Groundwater Sustainability Agency(ies)—Referring to SVGMD and Plumas County
 - Sub= SVGMD Board Subcommittee
- Note:** The highlighted sections below identify tasks that directly require engagement from the SVGMD Board of Directors over the next 5 months.
- C= Consultant(s)
 - DWR= California Department of Water Resources
 - TSS= Technical Support Services Program (DWR)
 - PW= Public Workshop

Month/Year	Meetings/Milestones	Key Topics & Actions
January 2019	<ul style="list-style-type: none"> • GSP Project Team (monthly) 	<ol style="list-style-type: none"> 1. PT: Clarify GSP Work Plan priorities and next steps 2. PT: Refine work plan to incorporate draft GSP development progress
February 2019	<ul style="list-style-type: none"> • GSP Project Team (monthly) • SVGMD Board Meeting (monthly) • Tribal-FS Meeting 	<ol style="list-style-type: none"> 1. GSA: Approve coordination agreement between SVGMD and Plumas County 2. PT: Review GSP draft sections (Chapter 1 and Land Subsidence) to help identify data, technical, and resource gaps to inform development of GSP grant application work plan.
March-April 2019	<ul style="list-style-type: none"> • GSP Project Team (monthly) • SVGMD Board Meeting (monthly) • SVGMD Board Planning Subcommittee • Initiating Planning Grant 	<ol style="list-style-type: none"> 1. C: Bachand & Associates recharge study report findings presentation to SVGMD Board of Directors at March board meeting. 2. PT/GSA: GSP Project team present preliminary subsidence presentation to the SVGMD Board of Directors at April Board meeting.
May-August 2019	<ul style="list-style-type: none"> • GSP Project Team (monthly) • SVGMD Board Meeting (monthly) • SVGMD Board Planning Subcommittee <ul style="list-style-type: none"> ○ Defining Programs and Priorities for funding • Finalizing Planning Grant 	<ol style="list-style-type: none"> 1. DWR: Release of Project Solicitation Package (PSP) for GSP grant application expected in May. 2. PT: GSP Project Team review draft PSP and refine work plan for completion of proposal (see figure 1 on page 4). 3. PT with Burkhard Bohm: Compile existing basin setting information (technical information associated with basin conditions) to compare to GSP requirements and identify data, technical, and resource gaps to inform development of GSP grant proposal. 4. C/PT/Sub: Establish schedule for subcommittee meetings (to begin meeting in May). 5. PT/Sub/GSA: Present PSP requirements and activities

Month/Year	Meetings/Milestones	Key Topics & Actions
		<p>and timeline for completion of proposal to SVGMD Board of Directors at May Board meeting.</p> <ol style="list-style-type: none"> 6. PT: Prepare draft comments to DWR on draft PSP 7. C/PT: Release of groundwater study report and GSP Project Team review (May). 8. PT/GSA: Present draft PSP comments to SVGMD at May board meeting and receive input. 9. PT/GSA: Incorporate SVGMD and Plumas County comments and finalize comments on draft PSP and submit to DWR. 10. DWR: Release Phase 2 final Basin Prioritization results. 11. DWR: Release of final PSP for GSP grant program (expected late July). 12. C/PT/GSA/Sub: Draft GSP grant proposal, present progress updates and receive input and comments at SVGMD monthly board meetings and subcommittee meetings, incorporate GSA input, and submit proposal (expected submission deadline: late August). 13. TSS (GSA/DWR): Complete agreement with landowners for entry permit on land for TSS multi-completion well installation 14. TSS (GSA/DWR): Complete environmental documentation for TSS multi-completion well application 15. TSS (DWR): Receive clearance from Caltrans for encroachment permit for TSS multi-completion well application. 16. TSS (GSA) Secure/record access easement from landowner to TSS multi-completion well. 17. TSS: Begin construction on multi-completion well.
September-December 2019	<ul style="list-style-type: none"> • GSP Project Team (monthly) • SVGMD Board Meeting (monthly) 	<ol style="list-style-type: none"> 1. DWR: announcement of GSP Grant Awards (October) 2. GSA/PT: Draft and review RFP for any needed GSP consulting services as per the GSP grant application and determine process for consultant selection
November-December 2019	<ul style="list-style-type: none"> • GSP Project Team • SVGMD Board Meeting • Public Workshop (tentative) 	<ol style="list-style-type: none"> 1. GSA/DWR: If awarded GSP grant, work with DWR on contracting 2. GSA/PT: Finalize RFP for consulting services and release 3. GSA/PT: Respond to consulting team questions before proposal submission 4. GSA: Receive consultant proposals, conduct interviews and select consultant(s) 5. PW: Tentative Public workshop (content of workshop TBD)
January-March 2020	<ul style="list-style-type: none"> • GSP Project Team (note-committee structure may be redefined at this point) • SVGMD Board Meeting 	<ol style="list-style-type: none"> 1. GSA: Contract with selected consultant(s) 2. C/PT/GSA: Monitoring protocols 3. C/PT/GSA: Maps 4. C/PT/GSA: Water Resource Monitoring and Management Programs 5. DWR: Release Project Solicitation Package for GSP Implementation Grants.

Month/Year	Meetings/Milestones	Key Topics & Actions
April-June 2020	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting ● SGMA Public Workshop 	<ol style="list-style-type: none"> 1. C/PT/GSA: Description of Plan Area 2. C/PT/GSA: Draft Basin Setting results 3. C/PT/GSA: Monitoring networks 4. PW: Stakeholder feedback on basin conditions/undesirable results
July-September 2020	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting 	<ol style="list-style-type: none"> 1. C/PT/GSA: Land use elements and plans 2. C/PT/GSA: Additional GSP Elements including, but not limited to, impacts on Groundwater Dependent Ecosystems
October-December 2020	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting ● SGMA Public Workshop 	<ol style="list-style-type: none"> 3. C/PT/GSA: Representative monitoring 4. C/PT/GSA/PW: Sustainability goal 5. C/PT/GSA/PW: Measurable objectives 6. C/PT/GSA/PW: Minimum Thresholds
January-March 2021	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting ● SGMA Public Workshop 	<ol style="list-style-type: none"> 1. C/PT/GSA: Assessment and improvement of monitoring network 2. C/PT/GSA: Sustainability goal 3. C/PT/GSA: Measurable objectives (what conditions are desirable) 4. C/PT/GSA: Minimum Thresholds (what conditions are unacceptable) 5. C/PT/GSA/PW: Projects and Management Actions
April-June 2021	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting ● SGMA Public Workshop 	<ol style="list-style-type: none"> 1. C/PT/GSA: Projects and Management Actions 2. C/PT/GSA/PW: Draft GSP for public Comment
July-September 2021	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting 	<ol style="list-style-type: none"> 1. C/PT/GSA: Response to public comments
October-December 2021	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting ● SGMA Public Workshop 	<ol style="list-style-type: none"> 1. C: Incorporate public comments and prepare final review draft GSP 2. PT/GSA: Final review of GSP 3. C: Prepare final draft of GSP 4. GSA: GSAs adopt resolutions in support of GSP
January 2022	<ul style="list-style-type: none"> ● GSP Project Team ● SVGMD Board Meeting 	<ol style="list-style-type: none"> 1. GSA: Submit GSP to DWR via SGMA Portal

Figure 1. GSP Grant Application Preparation Timeline

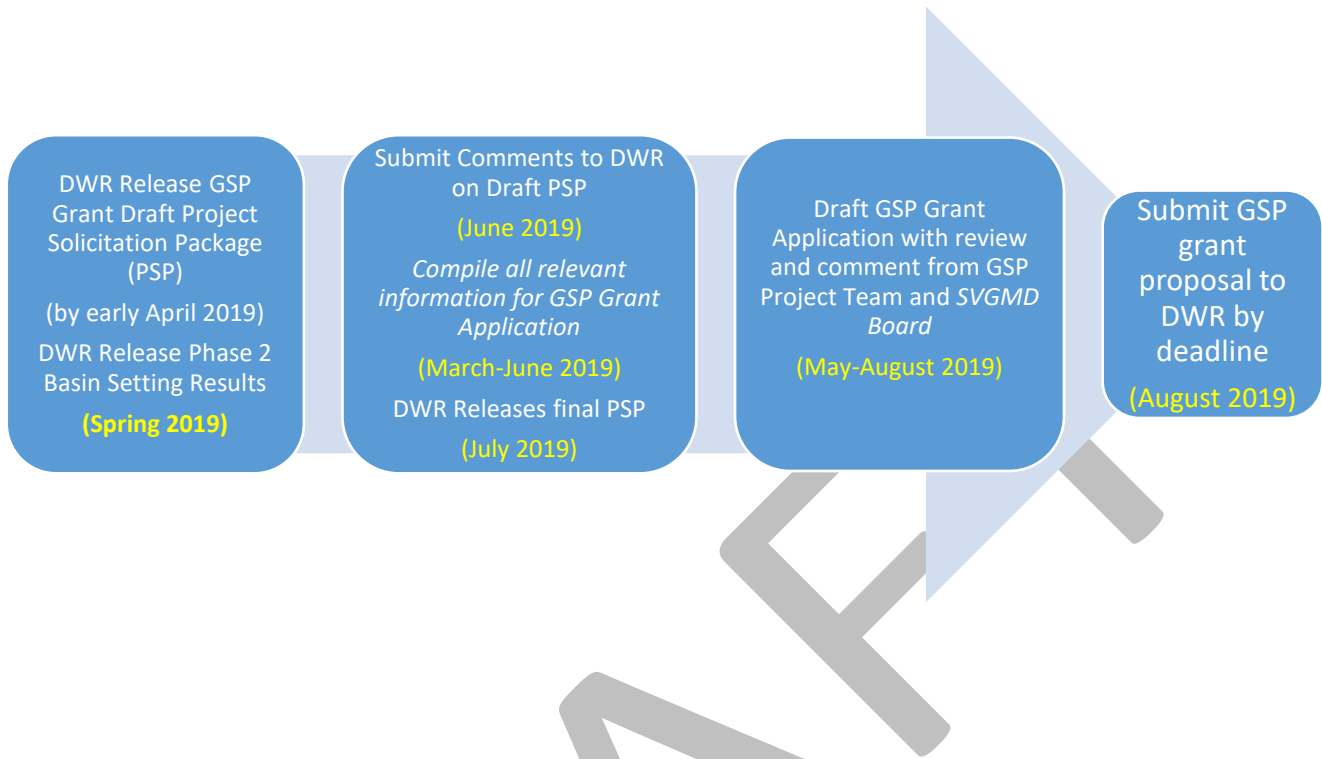


Figure 2. GSP Planning Grant Application Organization

Planning Grant Application Organization

